

Work Order ID 100235***100235***

Page 1

Monday, April 22, 2013 8:42:00 AM

Item ID: D2739

Accept

N900040100Setup Start ***NS1***

Revision ID:

Item Name: 350 I Beam

Stop ***NS2***

Start Date: 4/22/2013 Start Qty: 4.00

4

Cust Item ID:

Required Date: 4/26/2013 Req'd Qty: 4.00

4

Customer:

Reference:

Approvals:

Process Plan: PLDate: 13-04-22

Tooling:

Date:

Run Start ***NR1***

QC:

Date:

SPC (Y/N):

Date:

Stop ***NR2***Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

Draw Nbr

Revision Nbr

D2739

Rev E

100

0.00

100

Skidtubes

Skidtubes

Memo

0.00

Skidtubes

1-Cut D2600-5 to length as per Dwg D2739.
2-Drill pilot holes in web using drilling Jig DT8162 as per Dwg D2739
3-Use uni-bit to open holes to finish size as per Dwg D2739.
4-Bevel Fwd end of extrusion and Deburr holes and ends.
5-Deburr

- DC 13/04/22

120

Chemical Conversion Coat per QSI005 4.1

0.00

120

HandFinish

Memo

0.00

Hand Finishing

- DC 13/04/22

Work Order ID 100235

Monday, April 22, 2013 8:42:00 AM

100235

Page 2

Item ID: D2739

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: 350 I Beam

Start Date: 4/22/2013 Start Qty: 4.00

4

Cust Item ID:

Required Date: 4/26/2013 Req'd Qty: 4.00

4

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

130

QC5- Inspect part completeness to step on W/O

0.00

130

QC

Memo

0.00

Quality Control

4 0 13-04-22 DAS 18 9-89

140

Identify as per dwg & Stock Location: 4/6-

0.00

140

Packaging

Memo

0.00

Packaging

DC 13/04/22

150

QC21- Final Inspection - Work Order Release

0.00

150

QC

Memo

0.00

Quality Control

13/4/25

RB-04-24

NCR: Yes / No

WORK ORDER NON-CONFORMANCE / UPDATE

DQA: _____ Date: _____

QA Closed: _____ Date: _____

Work Order: _____ Part No. _____ NCR No. _____				DISPOSITION Rework <input type="checkbox"/> Scrap <input type="checkbox"/> Use-as-is <input type="checkbox"/> Work Order Update <input type="checkbox"/>		AGAINST DEPARTMENT/PROCESS <div style="display: flex; justify-content: space-between;"> <div> Skid-tube <input type="checkbox"/> Machining <input type="checkbox"/> Thermoforming <input type="checkbox"/> Large Fab <input type="checkbox"/> </div> <div> Crosstube <input type="checkbox"/> Small Fab <input type="checkbox"/> Finishing <input type="checkbox"/> Composite <input type="checkbox"/> </div> <div> Water Jet <input type="checkbox"/> Prod. Eng. Coord. <input type="checkbox"/> Rec/Store/Packaging <input type="checkbox"/> Supplier <input type="checkbox"/> </div> <div> Engineering <input type="checkbox"/> Quality <input type="checkbox"/> Other <input type="checkbox"/> </div> </div>					
Root Cause	Date	Step	Qty	Description of work order update or Non-conformance	Initial Chief Eng	Action Description	Sign & Date	Verification	QC Inspector		
Doc/Data											
Equip/Tooling											
Operator											
Material											
Setup											
Other											
Process											
Supplier											
Training											
Unapproved											

FAULT CATEGORY				
Landing Gear <input type="checkbox"/> Bending <input type="checkbox"/> Centre Not Concentric to O/S <input type="checkbox"/> Cracks <input type="checkbox"/> Crushed/Crimped <input type="checkbox"/> Cuffs <input type="checkbox"/> Heat Treat <input type="checkbox"/> Inspection Strip in Tube <input type="checkbox"/> Ripples in Bend <input type="checkbox"/> Torque Waves in Extrusion <input type="checkbox"/> Turning Sequence <input type="checkbox"/> Wave/Twist in Tube	General <input type="checkbox"/> Bend <input type="checkbox"/> BOM/Route <input type="checkbox"/> Broken/Damaged <input type="checkbox"/> Burrs <input type="checkbox"/> Contamination <input type="checkbox"/> Countersink <input type="checkbox"/> Cut Too Short <input type="checkbox"/> Drill Holes <input type="checkbox"/> Drawing <input type="checkbox"/> Finish <input type="checkbox"/> Folio	<input type="checkbox"/> Grain <input type="checkbox"/> Hardware <input type="checkbox"/> Inspection Incomplete <input type="checkbox"/> Instructions Incomplete/Unclear <input type="checkbox"/> Maintenance <input type="checkbox"/> Mislabeled <input type="checkbox"/> Misread <input type="checkbox"/> Offset <input type="checkbox"/> Out of Calibration <input type="checkbox"/> Out of Sequence <input type="checkbox"/> Outside Dimensions	<input type="checkbox"/> Ovalized <input type="checkbox"/> Over/Under tolerance <input type="checkbox"/> Part Incorrect <input type="checkbox"/> Part Lost/Missing <input type="checkbox"/> Part Moved <input type="checkbox"/> Positioned Wrong <input type="checkbox"/> Power Loss/Surge <input type="checkbox"/> Pressure/Forced <input type="checkbox"/> Temperature/Cure <input type="checkbox"/> Weld <input type="checkbox"/> Wrong Stock Pulled <input type="checkbox"/> Other	

Picklist Print

Monday, April 22, 2013 8:42:41 AM

Page 1

Work Order ID: 100235

100235

Parent Item: D2739

D2739

Parent Item Name: 350 I Beam

Start Date: 4/22/2013

Required Date: 4/26/2013

Start Qty: 4.00

Required Qty: 4.00

Comments:

IPP Rev: C02.11.28ReformatKJ

IPP Rev: D 06-03-21 As Per Rev C JLM

IPP Rev: E 07-07-28 As per Rev D JLM Verified By: IPP Rev:F

10.11.02 as per revE DD verf:EC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

D2600-5-108

Manufactured

No

Each

113.0000

4

D2600-5-108

**

DC 13/04/22

Extrusion 'I Beam' thin

Location

Loc Qty

Loc Code

LG

113



73909

2


90684

111

4

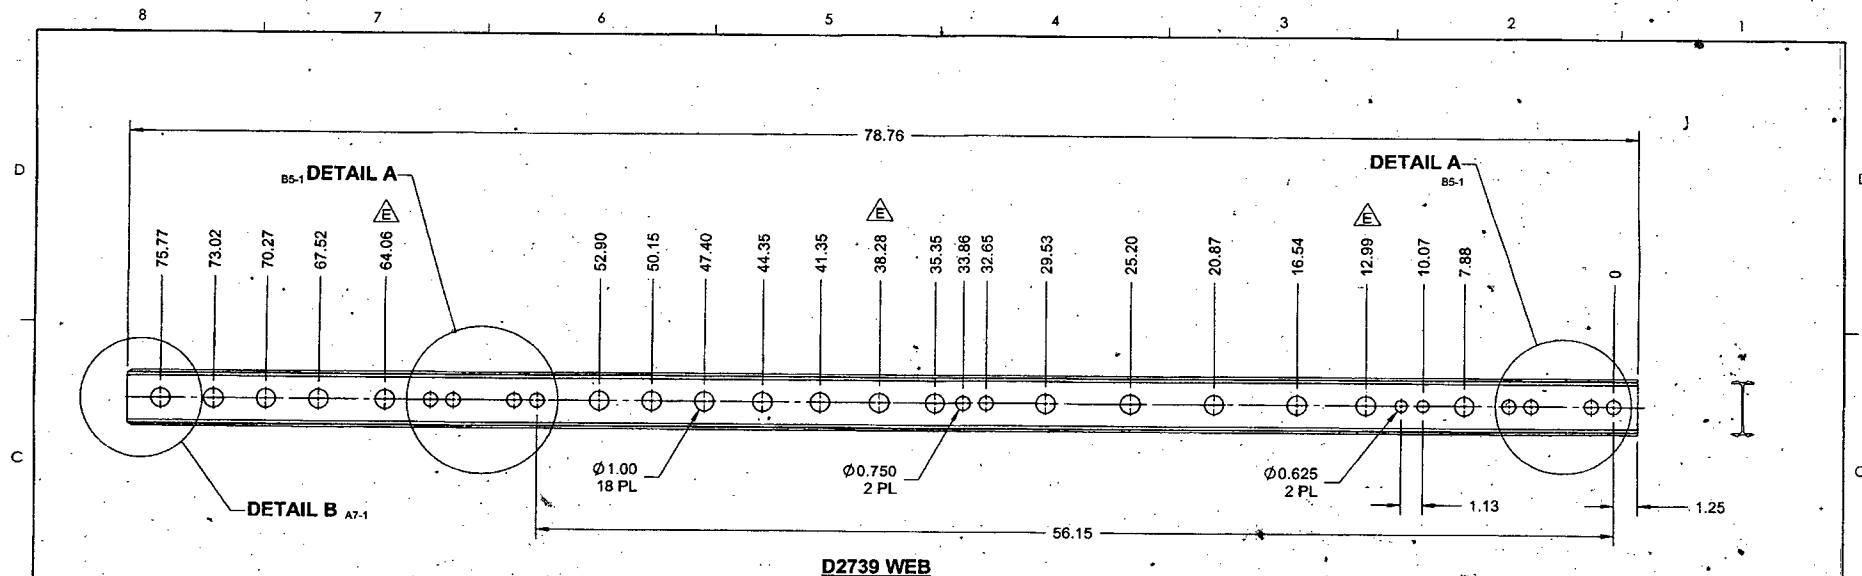

DETAIL B
SCALE 3X C7-1



DETAIL A
SCALE 3X D7-1, D2-1

NOTES:

- 1) MATERIAL: MAKE FROM D2600-5 EXTRUSION
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: DART P/N "D2739" AND B/N PER DART QSI 044 6.1
- 7) WEIGHT: 3.41 lbs

E	ADD/MOVE HOLES FOR D4154 WEARPLATE; 38.28 WAS 38.35 (D5-1), 64.06 WAS 64.77 (D7-1), ADD HOLE (D3-1)	CP	10.10.08
D	ADD BEVEL TO FWD END; ADD DETAIL B.	CB	07.05.29
C	ADD/MOVE HOLES FOR COMPATIBILITY WITH APICAL FLOATS	PH	06.01.05
B	CHANGE HOLES FOR COMPATIBILITY WITH AIRCRUISER FLOATS	CP	98.11.18
A	NEW ISSUE	DS	98.04.16
REV.	DESCRIPTION	BY	DATE
DESIGN	DS	DART AEROSPACE USA, INC. PORT HADLOCK, WA	
DRAWN	JP		
CHECKED	JP	DRAWING NO.	REV. E
MFG. APPR.	JP	D2739	SHEET 1 OF 1
APPROVED	JP	TITLE	SCALE
DE APPR.	JP	WEB	NTS
DATE	10.10.08	COPYRIGHT © 1998 BY DART AEROSPACE USA, INC. THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMERCIALITY TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE USA, INC.	
